
• Project Status

Round Elementary projects have started

- Moving company has moved media center to temporary storage (hallways, classrooms, storage units).
- Demolition is underway in building
 - removal of boilers, gym air handler, classroom casework, courtyard and media center

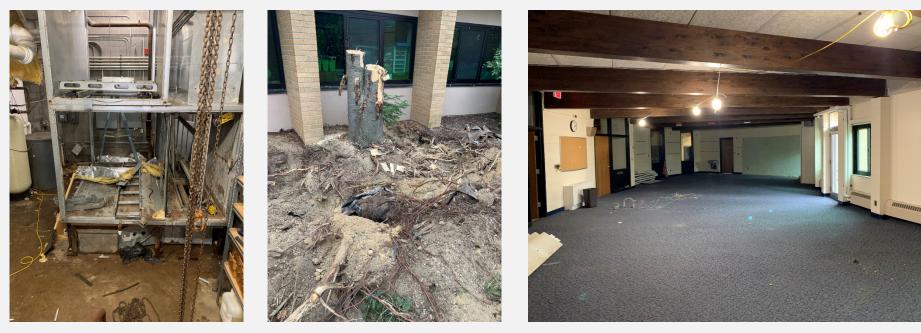

• Project Status

Village Elementary projects have started

- Moving company has moved media center to temporary storage (gym).
- Demolition is underway in building
 - removal of boilers, classroom casework, classroom lights, courtyard and media center







• Project Status

Lakes Elementary projects have started

- Moving company has moved media center to temporary storage (gym).
- Demolition is underway in building
 - media center



• Project Status

Creekside Elementary projects have started

- Moving company has moved media center to temporary storage (gym).
- Demolition is underway in building
 - media center



• Project Status

Robotics Center

- Construction starting approximately August 20th
- Construction ending approximately March 2022
- Still working with robotics members on furniture selection
- Materials for construction are being delayed due to production issues and transportation (Due to COVID)
 - Meeting school start dates are critical
 - Creating backup plans in case there are issues meeting deadlines. Such as:
 - Substituting materials
 - Scheduling work on non-school days/times (weekends / after hour shifts)

Next Round of Projects

Auxiliary Athletic Field – (potential board approval July)

- Currently performing cost estimation
- Tentatively site work starting December 1st 2021

Review of Summer 2022 projects- (potential bidding November 2021)

- Collaboration center at Ore Creek and Farms
- Classroom renovations, mechanical and electrical renovations at Ore Creek and Farms
- Athletic facilities upgrades at HS main stadium, Baseball and Softball fields.
