

Project Status

Round Elementary

- STEM Center installing lights, cabinets, & carpet. Furniture install started August 5th
- Mechanical Work installing boilers and pumps
- Gym installing gym floor August 6th, installing basketball hoops
- Building cleaning is now ongoing







Project Status

Village Elementary

- STEM Center installing lights, cabinets, & carpet. Furniture install started August 5th
- Mechanical Work installing boilers
- Classroom lighting complete
- K-Restrooms walls installed, walls painted
- Building cleaning is now ongoing








Project Status

Lakes Elementary

- STEM Center – installing lights, cabinets, & carpet. Furniture install started August 5th
- Kitchen Make Up Unit Completed
- Building cleaning is now ongoing

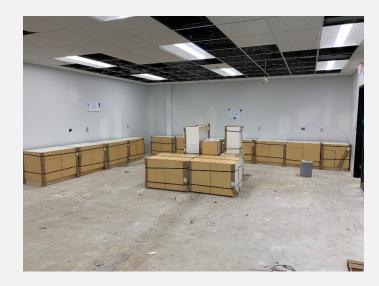





Project Status

Creekside Elementary

- STEM Center – installing lights, cabinets, & carpet. Furniture install started August 5th
- Secured entry door—installing overhang, brick work, installing lighting
- Building cleaning is now ongoing



413

Board Bond Update – August 2021

Project Status

Robotics Center

- Demolition started on August 4th
- Construction ending approximately March 2022
- Furniture selection completed
- Materials for construction are being delayed due to production issues and transportation (Due to COVID)
 - Meeting school start dates are critical
 - Creating backup plans in case there are issues meeting deadlines. Such as:
 - Substituting materials
 - Scheduling work on non-school days/times (weekends / after hour shifts)

Next Round of Projects

Auxiliary Athletic Field – (potential board approval November)

- Changes were made to design due to cost estimates over budget
- Tentatively site work starting January February 2022
- Tentatively opening August 2022

Review of Summer 2022 projects— (potential bidding November 2021)

- Collaboration center at Ore Creek and Farms
- Classroom renovations, mechanical and electrical renovations at Ore Creek and Farms
- Athletic facilities upgrades at HS main stadium, Baseball and Softball fields.
