



# Board Bond Update – November 2021

- **Project Status**

## Round Elementary

- Contractors are working punch list items. Estimated completion Nov 29<sup>th</sup>
- Owner training occurred on the RTU and boilers with maintenance, dishwasher with Food Service
- Remaining items – Walk in Cooler/Freezer (Sinking Fund)

## Village Elementary

- Contractors are working punch list items. Estimated completion Nov 29<sup>th</sup>
- K-Restrooms – are open and in use
- Remaining items – Gym roof (roof membrane is onsite, insulation is delayed and installation is unknown at this time)



# Board Bond Update – November 2021

- **Project Status**

## Lakes Elementary

- Contractors are working punch list items. Estimated completion Nov 29<sup>th</sup>

## Creekside Elementary

- Contractors are working punch list items. Estimated completion Nov 29<sup>th</sup>
- Remaining items – Exterior Doors are being installed, 2 door frames were damaged in shipping, waiting on replacements.





# Board Bond Update – November 2021

- **Project Status**

Robotics Center – tentative completion March 2022

- Steel installed, roof decking installed,
- Masons working on addition block/brick
- Plumbing roughed in / compressed air lines installed
- HESSC – boiler replacement is underway





# Board Bond Update – November 2021


- **Project Status**

- Auxiliary Athletic Field – (board approval November 8, 2021)

- Site work starting January – February 2022
    - Opening August 2022
    - Synthetic Turf Field
      - Lined for the following sports
        - Football
        - Men's and Women's Lacrosse
        - Soccer
        - Field Hockey
    - Press box
    - Field Lighting
    - Concessions and Restrooms building (servicing Auxiliary Stadium and HS tennis courts)
    - Additional parking added to service Auxiliary Stadium and HS tennis courts
    - Walking path connected to Hartland road's path




# Board Bond Update – November 2021

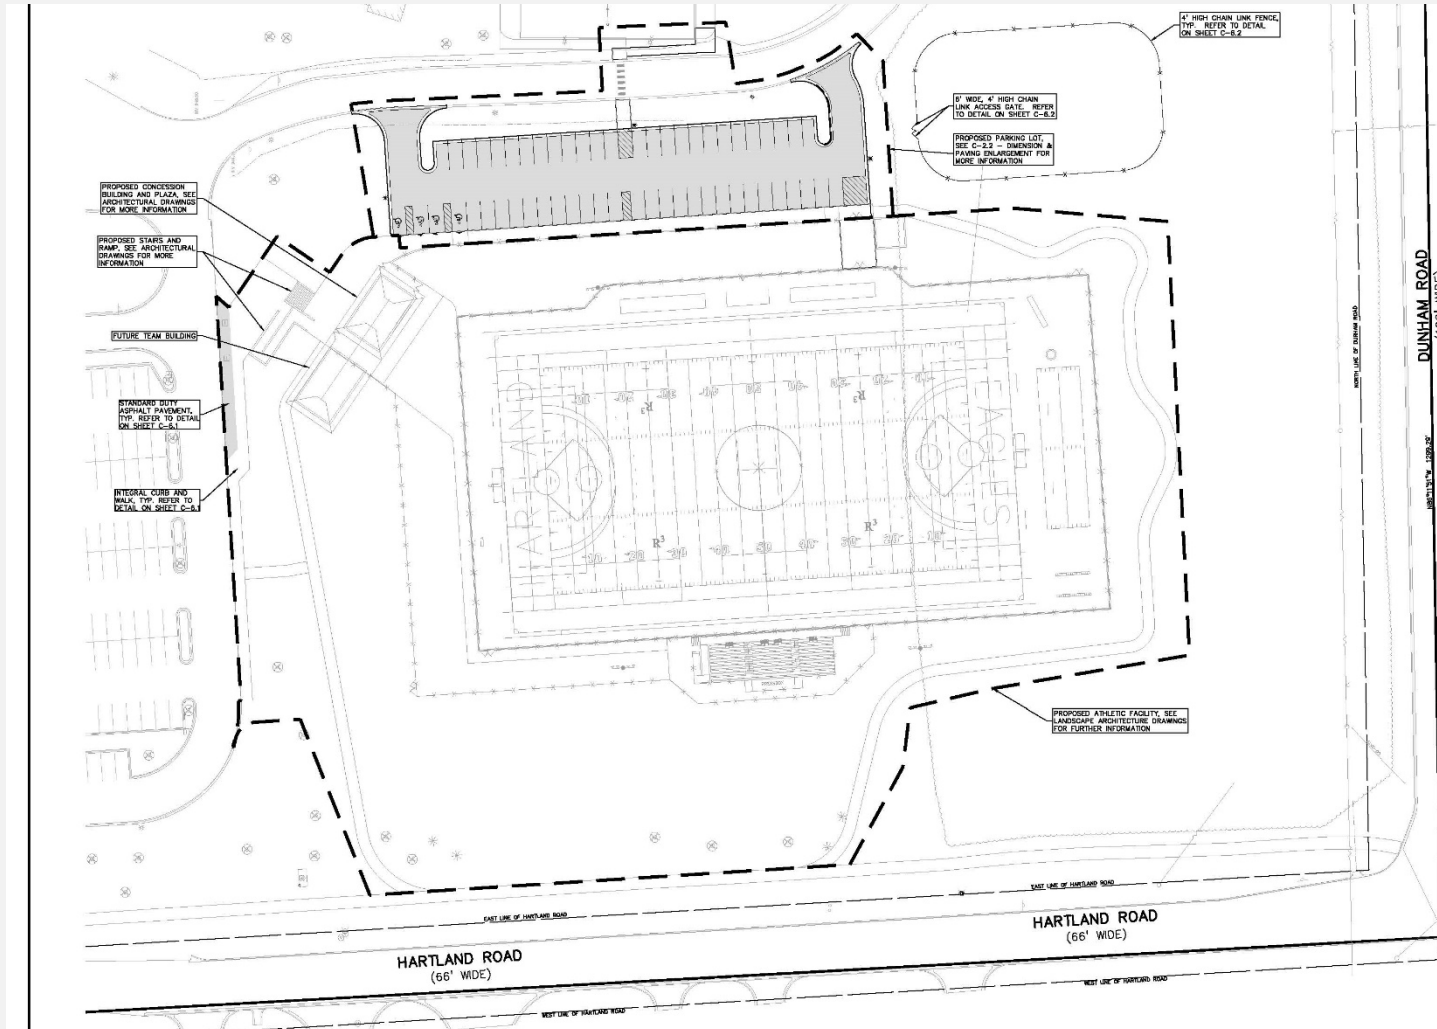



# Board Bond Update – November 2021

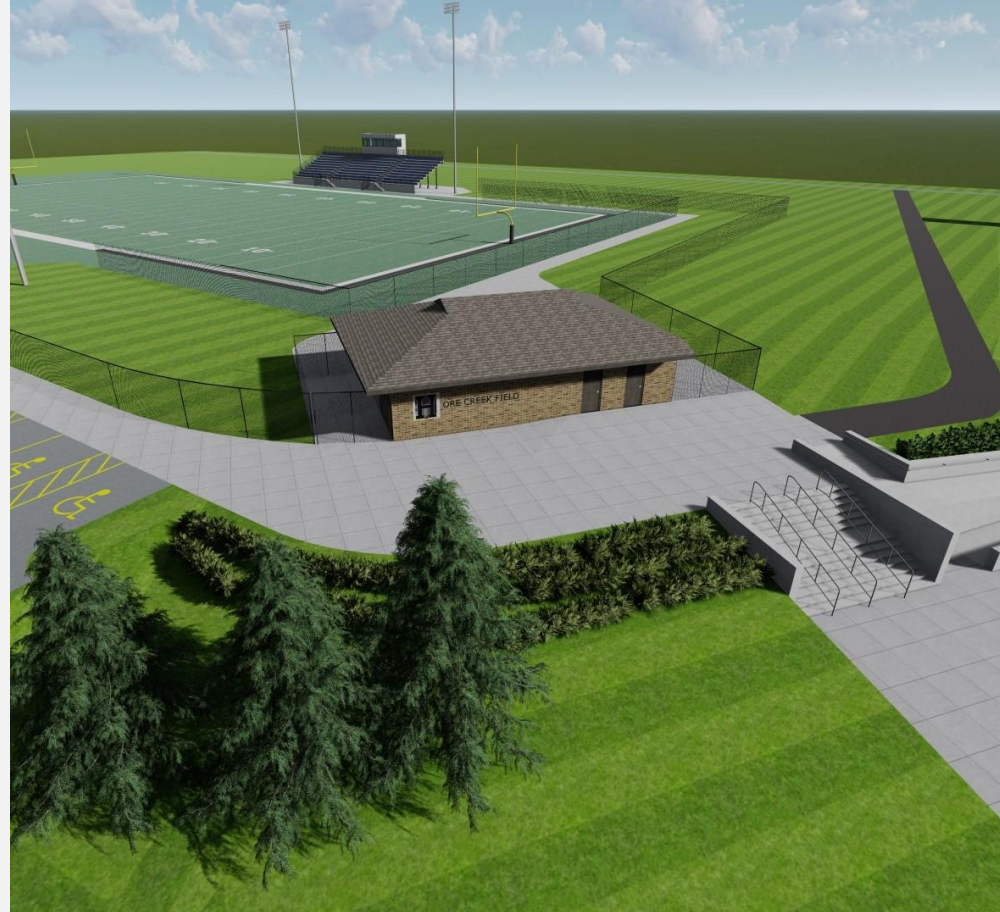

Entrance Rendering



# Board Bond Update – November 2021

- **Next Round of Projects**

Review of Summer 2022 projects– (potential bidding November 2021)

- Reviewing renovations with building principals (Farms and Ore Creek)
  - Selecting interior finishes (cabinets)
  - Selecting carpet styles and colors
- Reviewing Athletic facilities upgrades with Athletic Director
  - Selecting press box style
  - Selecting bleacher style and seating capacity
  - Reviewing lock room sizing and layout
