

# Board Bond Update – January 2022

- **Project Status**

## Round Elementary

- Contractors are working on final punch list items.
- Remaining items – Walk in Cooler/Freezer (Sinking Fund), poured the concrete pad

## Village Elementary

- Contractors are working on final punch list items.
- Remaining items – Gym roof (roof membrane and insulation onsite, install spring break)

## Lakes Elementary

- Contractors are working on final punch list items.



# Board Bond Update – January 2022

- **Project Status**

## Creekside Elementary

- Contractors are working on final punch list items.
- Remaining items – Exterior Doors are onsite waiting on a good time to install them, secured vestibule was finished over the holiday break. We will be switching the “buzzer” system over in the next week or two.



# Board Bond Update – January 2022

- **Project Status**

Robotics Center – tentative completion March 2022

- Roof fascia, curbing installed and roofing membrane installed
- Masons working on addition block/brick, interior rooms, exterior walls insulated
- Demoed interior walls for new hallway windows and doorway and reconstructing




# Board Bond Update – January 2022

- **Project Status**

  - Auxiliary Athletic Field

    - Contracts being issued
    - Permits being issued
    - Site work starting January – February 2022
    - Opening August 2022

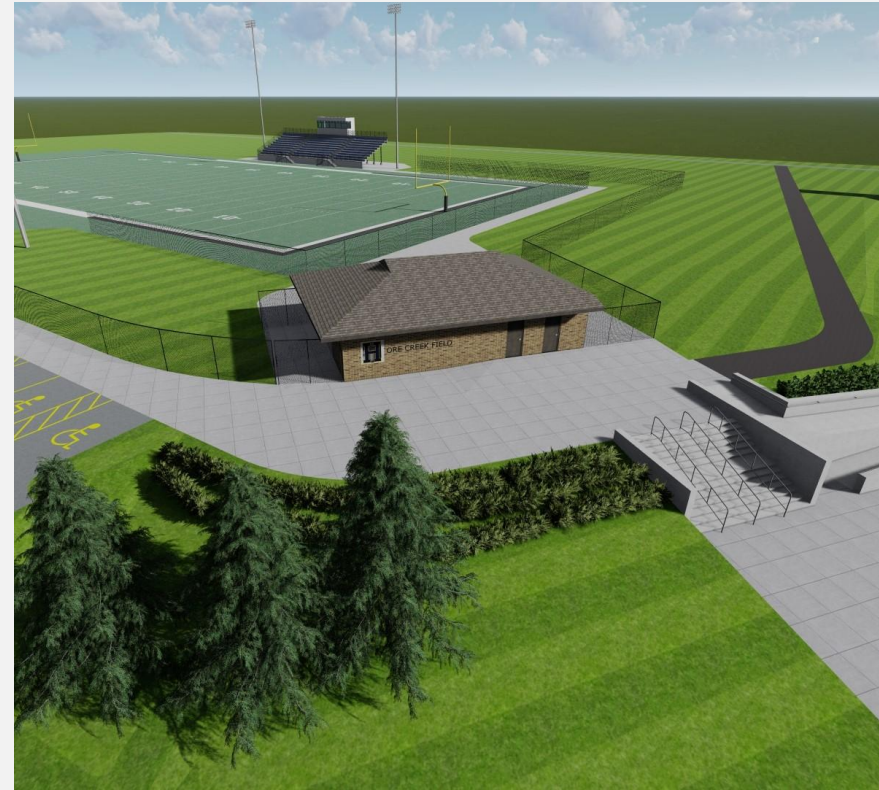

Entrance Rendering



# Board Bond Update – January 2022

- **Next Round of Projects**

Summer 2022 projects– (BP#5A approval at January board meeting)

- Ore Creek –
  - Building carpet replacement
  - Exterior window replacement
  - Stage curtain replacement
  - Fire Alarm replacement (sinking fund)
- Districtwide Video Surveillance upgrades -



# Board Bond Update – January 2022

- **Next Round of Projects**

Summer/Fall 2022 projects– (bidding BP#5B January 2022)

- Athletic field renovations
  - Adding a team room to the main stadium which includes secondary concession, and storage
  - Renovation of Baseball and Softball complex
    - Adding a press box for BB and SB
    - Adding storage for BB and SB
    - Adding restrooms to service BB and SB
    - Adding a protective netting to SB
- Senior Center upgrades
  - Restroom renovations
  - Entrance Door
  - Sidewalk hand railing
