



Board Bond Update – February 2022

- **Project Status**

Creekside Elementary, Round Elementary, Village Elementary and Lakes Elementary

- Contractors are working on final punch list items. – Close out materials
- Round's remaining item – Walk in Cooler/Freezer (Sinking Fund), poured the concrete pad (March)
- Village's remaining item – Gym roof (roof membrane and insulation onsite, install spring break)
- Creekside's remaining item – Main and bus exterior doors are onsite, requires 2-3 days to perform the work. Install scheduled for spring break.


Board Bond Update – February 2022

- **Project Status**

Robotics Center – tentative completion March 2022

- Interior walls completed, addition's floor poured, mezzanine steel installed
- Installing mechanical duct work – waiting on roof top unit (March)

HESSC Boilers – 3 running, other 3 start up scheduled for the Feb. 16th

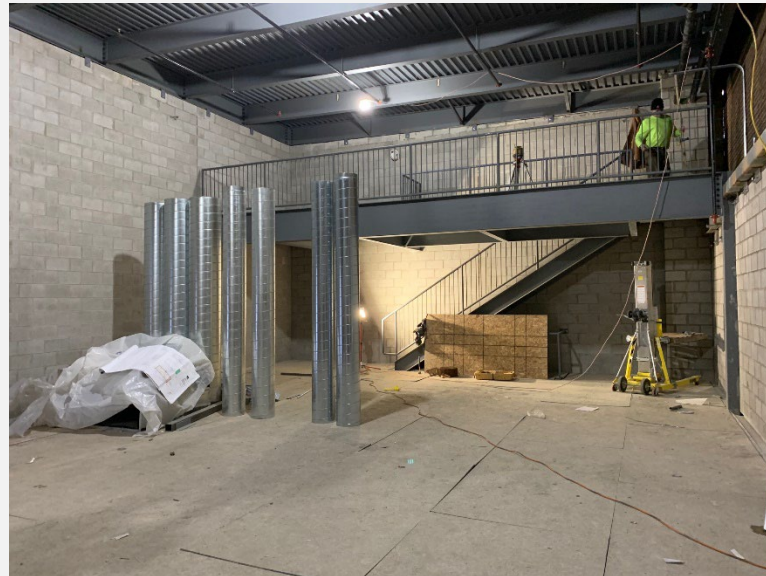




Board Bond Update – February 2022

- **Project Status**

- Auxiliary Athletic Field

- Contracts were issued
 - Permits being issued
 - Site work starting February 2022 – starting with clearing trees and installing soil erosion fencing
 - Opening Fall 2022

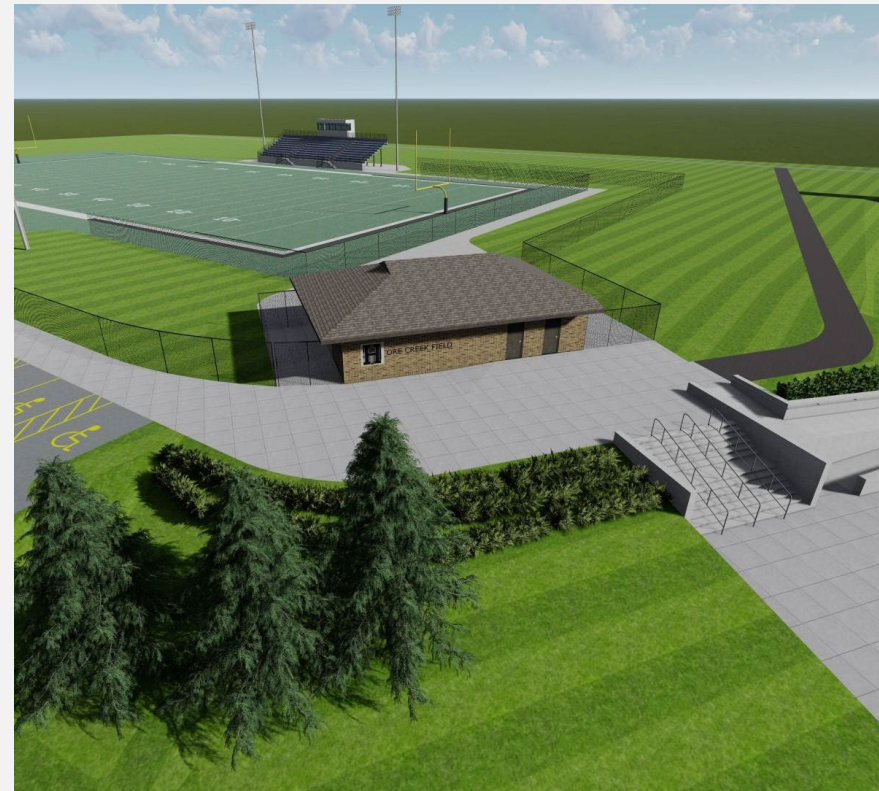

Entrance Rendering



Board Bond Update – February 2022

- **Next Round of Projects**

Summer 2022 projects

- Ore Creek – building carpet replacement, exterior window replacement, stage curtain replacement, fire alarm replacement (sinking fund)
 - Contracts being issued
 - Permits being issued
 - Reviewing color and product submittals
- Districtwide Video Surveillance upgrades –
 - Reviewing scope with contractor
 - Work will be performed on 2nd shift (after school) and over spring break



Board Bond Update – February 2022

- **Next Round of Projects**

Summer/Fall 2022 projects—

- Bids were received on February 10th, district reviewing pricing
- Athletic field renovations
 - Adding a team room to the main stadium which includes secondary concession, and storage
 - Renovation of Baseball and Softball complex
 - Adding a press box for BB and SB
 - Adding storage for BB and SB
 - Adding restrooms to service BB and SB
 - Adding a protective netting to SB
- Senior Center upgrades
 - Restroom renovations
 - Entrance Door
 - Sidewalk hand railing
