



# Board Bond Update – April 2022

- **Project Status**

Creekside Elementary, Round Elementary, Village Elementary and Lakes Elementary

- Contractors are working on final punch list items. – Close out materials
- Round's remaining item – Walk in Cooler/Freezer (Sinking Fund), (May 2022)
- Village's remaining item – Gym roof (roof membrane and insulation onsite, moved to summer 2022)
- Creekside's remaining item – Main and bus exterior doors are onsite, (moved to summer 2022)




# Board Bond Update – April 2022

- **Project Status**

Robotics Center – tentative completion May 6, 2022

- Painting ceiling and walls completed
- Casework installed
- Ceiling lighting installed
- Exterior sidewalk installed

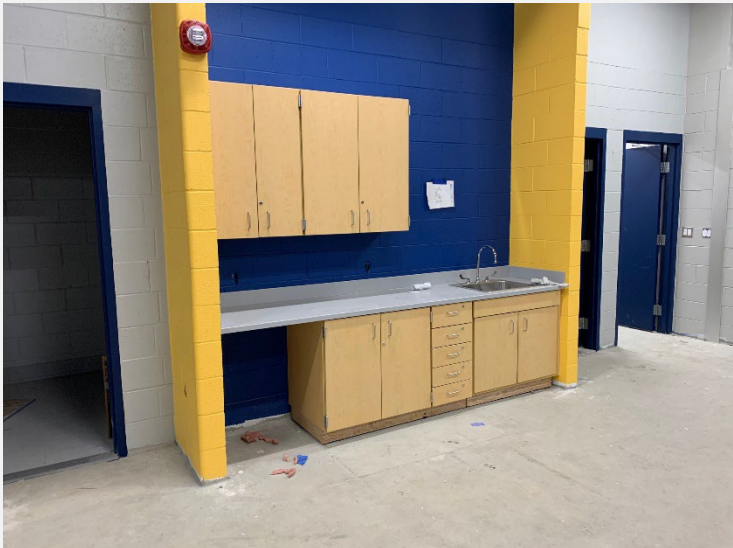



# Board Bond Update – April 2022

- **Project Status**

  - Auxiliary Athletic Field

    - Retention pond completed
    - Stripping of material is underway
    - Marking locations of lights and building





# Board Bond Update – April 2022

## Summer 2022 projects

- Ore Creek – building carpet replacement, exterior window replacement, stage curtain replacement, fire alarm replacement (sinking fund)
  - Working with contractors on timeline for work
- Districtwide Video Surveillance upgrades
  - Cabling installed at Farms over spring break
- Technology upgrades
  - Replacement of classroom displays at High School, Ore Creek and HESSC
  - Replacement of sound amplification at Ore Creek
- Senior Center upgrades - Restroom renovations, Entrance Door and Sidewalk hand railing
- Round Elementary - Domestic water piping replacement
  - Started on domestic water piping replacement in the tunnels – hanging next to current piping
