



# Board Bond Update – July 2022

- **Project Status**

Creekside Elementary, Round Elementary, and Village Elementary

- Round's remaining item – Walk in Cooler/Freezer is up and running (working on trim)
- Village's remaining item – Gym roof is 60% completed, finishing up this week
- Creekside's remaining item – Main and bus exterior doors installing over the next two weeks.





# Board Bond Update – July 2022

- **Project Status**

  - Robotics Center

    - Sections of the flooring had to be removed
      - Concrete infill completed and curing
      - Epoxy prep will start later this week
      - Epoxy will need to 1 week to cure before we can move in equipment and furniture.




# Board Bond Update – July 2022

- **Project Status**

## Auxiliary Athletic Field

- Concession stand footings exterior block walls are completed
- Main water line is tied in
- Parking lot curbs are installed and light poles are installed
- Turf – subbase and flat drain is all installed, electrical is installed, field goal poles are installed. Turf will be onsite this week and crews will start installing later this week
- Tentative timeline
  - Completion of field – August 12<sup>th</sup>

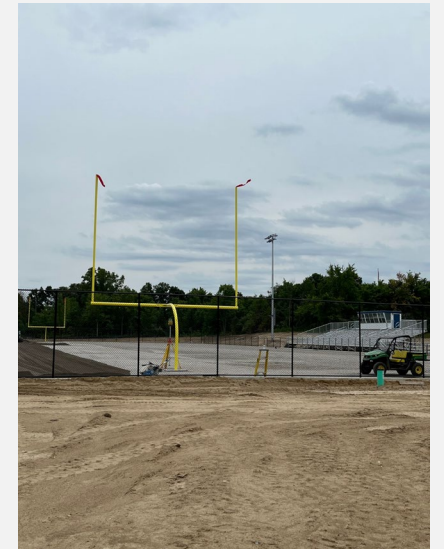



# Board Bond Update – July 2022

## Summer 2022 projects

- Ore Creek – building carpet replacement, exterior window replacement, stage curtain replacement, fire alarm replacement (sinking fund)
  - Fire alarm installation ongoing
  - Flooring LVT is installed , carpet is installed, working on installing base
  - Windows are being installed (approximately 2 weeks to complete)
- Senior Center upgrades -
  - Entrance door frame was installed July 12<sup>th</sup> (waiting on door)





# Board Bond Update – July 2022

## Summer 2022 projects

- Round Elementary - Domestic water piping replacement
  - Domestic water piping replacement in the tunnels – completed
  - Working on classroom and restroom replacement - 80 % complete
    - All restroom fixtures are being replaced





# Board Bond Update – July 2022

## Summer 2022 projects

- Districtwide Video Surveillance upgrades
  - Cameras and cabling 100% completed at Farms and Lakes
  - Cameras and cabling 80% completed at Round
- Technology upgrades
  - Replacement of classroom displays at High School is ongoing
  - Installation of classroom displays and sound amplification at Ore Creek will start after flooring is installed
